

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

August 20, 2009

#### ORR ELEMENTARY SCHOOL

##### DENSON

2<sup>nd</sup> Floor slabs are complete


Structural Steel erection continues in Areas B and C

Framing for drywall has started

Roof joists and deck are being installed


The next month's progress will be the completion of steel erection and roof deck. Continue framing and drywall for exterior and interior walls. Begin installation of fire sprinklers, ductwork, cable trays, roofing, electrical, and plumbing rough-in for the interior of the building.

A. W. ORR



FIRST FLOOR

NORTH KEY PLAN



SECOND FLOOR

NORTH KEY PLAN

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

August 20, 2009

#### CLARKSTON ELEMENTARY SCHOOL

##### RPR

Roofing installation at Area A is complete.

Brick work is continuing in Court Yard area.


Ductwork and all above ceiling work is nearing completion in Area A

Framing for interior and exterior walls is progressing well and Area A is almost complete.


Structural steel erection should be complete this month

Progress for the next month will be the completion of structural steel erection. Continuation of wall framing, roofing at Cafeteria and Gym, masonry along with mechanical, electrical, plumbing and technology rough-in. Start installation of Drywall in Areas A & B.

CLARKSTON



 NORTH KEY PLAN



 NORTH SECOND FLOOR KEY PLAN

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

August 20, 2009

#### WOODS ELEMENTARY SCHOOL

##### DENSON

Structural steel erection is continuing and 2<sup>nd</sup> floor decking is being installed


Final building slab pour was made on 8-12-09

First 2<sup>nd</sup> floor slab pour is scheduled for week of 8-17-09.


Framing for exterior walls has started

The next month's progress will be the completion of 2nd floor concrete slabs and completion of steel erection, installation of roof joists and deck, start framing interior walls, begin installation of fire sprinklers, ductwork, cable trays, electrical, and plumbing rough-in for the interior of the building.

ANDY WOODS



← NORTH  
FIRST FLOOR  
KEY PLAN



← NORTH  
SECOND FLOOR  
KEY PLAN

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

August 20, 2009

#### JONES/BOSHEARS SCHOOL

##### DENSON

2<sup>nd</sup> floor slab for Areas E & F is complete.

Framing for drywall is underway in Areas E & F.

Steel Erection at Area C is complete and has started in Area D



Masonry walls are complete at Gym

Metal building for Arena has been delivered to site, erection is underway.

First section of the Loop Road was poured on 8-12-09

Slab for Area B is scheduled to be poured on 8-20-09

The next month's progress will be the completion of the Arena structure and steel erection in Area C. Start steel erection in Area D and continue placing concrete on the loop road. Continuation the above ceiling rough-in for areas E & F. Roofing started at Areas E & F.

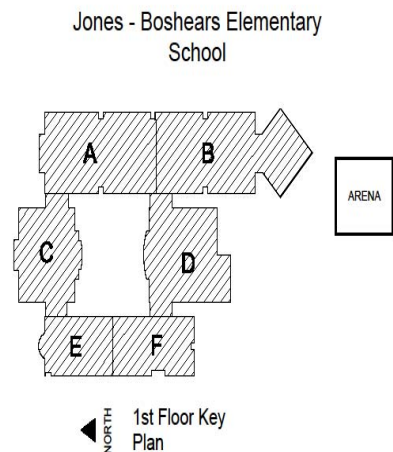

## **2008 BOND**

### **CONSTRUCTION PROGRESS REPORTS**

**August 20, 2009**

#### **GRIFFIN ELEMENTARY**

##### **DENSON**

The Contract for the new Athletic Field on the site of the Boys & Girls Club and the creation of a play field on the Dogan campus has been approved by the Board.

95% plans for the new School have been received. Final plans for bidding are due on or before 9-14-09.
